GROUSE
& COMPANY

JOINERY & INTERIORS
FOR BRITISH COUNTRY HOMES

PROJECT PROPOSAL

EAST MANOR FARM

BESPOKE STORAGE WITHIN ANGLED EAVES

PEPPARD COMMON - OXFORDSHIRE

2ND APRIL 2026

PROJECT UNDERSTANDING

A clear understanding of your brief

This proposal is based on our understanding of the space, the way it needs to function and the details discussed during our initial meeting. The aim is to create joinery that feels calm, practical and appropriate to the character of the house.

THE PROJECT

Bespoke eaves cupboards designed to make better use of the available space

Cabinetry kept visually light so it does not project too heavily into the room

Colour matched to the walls so the joinery blends naturally into the space

Concealed hinges and minimal detailing for a cleaner, more seamless look

KEY CONSIDERTIONS

Matching carefully with surrounding skirting moulding and original features when appropriate

Balancing useful storage with a calm, uncluttered feel in the room

Keeping materials, finishes and hardware choices clear and easy to approve

Resolving proportions, adjacent details and final sign-off before manufacture begins

The aim is a considered result that feels as though it has always belonged in the room.

Practical access, room protection and installation assumptions are outlined later in this proposal.

ABOUT GROUSE & CO

Thoughtful joinery for characterful homes

Grouse & Co was created for characterful countryside & heritage homes where standard solutions rarely feel quite right.

We believe good joinery should do more than fill a space. It should improve how a room works, feel natural within the property and carry a level of detail that can be appreciated every day.

Many clients find the process overwhelming: too many materials, too many hardware options, too much jargon and not enough clear guidance. Grouse exists to simplify that. We help shape the right route through design, specification, trusted makers, materials and installation, so the final result feels considered rather than complicated.

The “& Co” reflects how we work: bringing together good design judgement, practical craftsmanship, reliable suppliers and carefully chosen partners to deliver work that suits the home and the people living in it.

Grouse Standards

A curated route using handpicked colours, materials, hardware and details that we know work well together. This helps clients make confident decisions without being overwhelmed by endless options.

Fully Bespoke

For homeowners, architects and designers who want complete flexibility, we can develop a wider range of materials, finishes, features and custom details around the brief.

Considered Delivery

The final fit matters as much as the design. We place real importance on careful installation, clear communication, site protection and respect for the home throughout the process.

Two clear routes. One considered way of working.

OUR APPROACH

Clear thinking before careful making

Good joinery is shaped by the decisions made before anything is built.

Our approach is designed to remove uncertainty from the process. We simplify the choices, balance new work with the character of the home and resolve the important details before manufacture or installation begins.

This means fewer loose decisions, fewer surprises, and a calmer route from first ideas through to final fitting.

CLARITY EARLY ON CREATES A BETTER RESULT LATER

01

Simplify the Choices

We narrow the options to materials, finishes, hardware and details that suit the project, rather than overwhelming clients with endless possibilities.

02

Respect the Home

We balance modern function with the proportions, mouldings, existing details and natural character of the property.

03

Resolve before Build

We confirm measurements, drawings, specifications, finishes and key decisions before work moves into production or installation.

04

Considered Delivery

We think through access, protection, sequencing and installation carefully, so the work is delivered with as little friction and disruption as possible.

Fewer loose decisions. Better details. A calmer route to completion

GROUSE
& COMPANY

OUR PROCESS

A clear route from approval to installation

Once the proposal is approved, your project follows a defined sequence. Each stage is completed and signed off before the next begins, ensuring design, specification, production and installation are properly resolved before work is carried out.

IMPORTANT NOTES

Lead times
Lead times are confirmed at each stage and may vary depending on materials, complexity and supplier availability.

Changes and assumptions
Stage changes and late specification changes may affect lead times and cost.

Detailed assumptions, exclusions and site working notes are outlined later in this proposal.

1

Agreement & Deposit

Once the proposal is approved and the deposit is received, the project is scheduled and moves into the next stage.

2

Technical Site Measure

Final site dimensions are taken and any constraints, access points or existing are confirmed.

3

Design & Specification Sign-Off

Materials, colours, hardware, finishes and key details are finalised and agreed before drawings are released.

4

CAD Drawings & Production Pack

Technical drawings and production information are prepared for approval and manufacture.

5

Production, Assembly & Quality Control

Joinery is produced, checked and where needed pre-assembled or test fitted before installation.

6

Installation, Handover & Aftercare

The joinery is installed with care, final adjustments are completed and the client receives a handover and aftercare guidance.

PROJECT SCOPE / INVESTMENT

Scope & Investment Summary

This page summarises the proposed scope, pricing basis and base investment. Optional enhancements and specification upgrades are shown separately and only added if selected.

PROJECT DETAILS

Project: East Manor Farm
Client: Annie & William Bird
Site Address: Peppard Common, Oxfordshire
Proposal Ref: 135
Date Issued: 13th April 2026

PRICING BASIS

Prepared using the site visit, project brief, current measurements, and any drawings or information provided by the client, designer, architect or contractor.

Pricing may change if the design, drawings, materials, finishes, hardware, site conditions or agreed scope change.

SCOPE	DESCRIPTION	BASE INVESTMENT
Kitchen Joinery	Bespoke kitchen cabinetry, including island, painted shaker doors, internal storage, worktop coordination and installation.	£18,500
Utility/ Housekeeping Cupboards	Tall storage cupboards, luangdry housing, shelving and practical utility cabinetry.	£4200
Bedroom Fitted Wardrobes	Bespoe fitted wardrobes with hanging space, drawers and integrated storage	£7800

BASE INVESTMENT £30,500

STAGE 1 PAYMENT	VAT STATUS	VALIDITY
50% of final agreed investment	Not VAT Registered	30 Days from date of issue

PLEASE NOTE

A formal invoice and payment request will be issued separately through our payment system once the final agreed scope and any selected enhancements are confirmed.

GROUSE
& COMPANY

ENHANCEMENTS

Optional Enhancements

A curated selection of optional upgrades that can further enhance the function, finish and overall feel of the proposed joinery. Prices shown are additional to the base proposal investment.

ENHANCEMENT	ADDITIONAL INVESTMENT

Oak drawer internals

Solid oak dovetailed drawer boxes for a more premium internal finish and increased durability.

+ £450



Sensor lighting upgrade

Motion-activated LED lighting to wardrobes or cabinetry for a softer, more effortless user experience.

+ £250



Handle upgrade

Upgrade selected knobs or handles to an agreed premium hardware finish

+ £100



Internal accessories

Additional internal features such as velvet rails, jewellery trays, shoe storage or pull-out organisers

From +£180



PLEASE NOTE

Enhancements are optional and can be added prior to production release. Prices are additional to the base proposal investment and may change if the final specification changes. A revised investment summary will be issued once selections are confirmed.

PROGRAM & PAYMENT TERMS

A clear route from approval to completion

Our projects follow a staged structure that links approvals, production and payments to key milestones, helping keep the process clear, controlled and well-timed.

1	**Project Approval & Design Sign-Off** Deposit secures the project within our schedule and allows us to begin detailed CAD drawings, material selections and final approvals.	50%
2	**Production Release** Second payment is due prior to manufacture, outsourced production and major material orders, allowing the project to move into procurement, preparation and quality-controlled production.	40%
3	**Installation & Completition** Final balance due on completition of installation, final adjustments and handover.	10%

Each stage is defined and approved before moving forward, helping protect programme clarity, quality and cash flow.

- Programme timings are based on final design approval, supplier lead times and site readiness.
- Production cannot begin until final drawings, materials and specification are signed off.
- Variations or late changes may affect both programme and final contract value.
- A final invoice schedule is issued once the full package and any selected enhancements are agreed.

Three clear stages. One controlled route to completion

GROUSE
& COMPANY

ASSUMPTIONS, EXCLUSIONS & ACCEPTANCE

Assumptions & Exclusions

These assumptions and exclusions form the basis of our proposal and help ensure clarity for both parties before work moves into production and installation.

01 Scope & Basis

- Based on the information available at the time of issue.
- Only the works listed within the proposal are included.
- Changes to scope will be treated as variations.

02 Design & Approvals

- Final drawings, finishes, materials and hardware must be approved in writing before manufacture.
- Changes after approval may affect cost and programme.

03 Materials & Tolerances

- Natural variations in timber, veneer and painted finishes should be expected.
- Walls, floors and ceilings are assumed to be reasonably level, plumb and suitable unless otherwise stated.
- Hidden issues, unsuitable substrates or site defects are excluded unless specifically allowed for.

04 Access, Protection & Site Working

- Clear access is required on installation days.
- Room and access routes will be protected where practical, some residual dust is unavoidable.
- Larger items may be supplied in sections or assembled on site where access is restricted.
- Working hours are assumed to be 7:30am to 4:30pm unless otherwise agreed.

05 Programme, Trades & Variations

- Timings are based on final sign-off, supplier lead times and site readiness.
- Electrical, plumbing, glazing, decorating, flooring and other specialist are excluded unless stated.
- Additional works or late changes may affect both programme and contract value.

06 Warranty, Validity & Terms

- Workmanship is warranted for 12 months from completion.
- Quotation valid for 30 days from date of issue.
- Optional enhancements, upgrades and revisions may change the final agreed investment.

Acceptance

By signing below, the client confirms acceptance of the proposal scope, assumptions, exclusions, payment schedule and agreed next steps.

The project will be entered into the schedule once signed acceptance and the Stage 1 payment have been received.

CLIENT NAME _____

PROJECT _____

SIGNITURE _____ DATE _____

NEXT STEPS

01 Accept proposal

02 Confirm enhancements

03 Final invoice schedule issued

04 Stage 1 payment received and project scheduled

GROUSE & COMPANY

Thank you for giving Grouse & Co
the opportunity to prepare this proposal

After spending many years working abroad, I found that each time I came home I had a deeper appreciation for English culture, architecture, history and the character of the homes tucked away in our villages and countryside.

There is something special about these buildings. Their proportions, their imperfections, their materials and the quiet details shaped over time. They deserve work that respects what is already there, while carefully bringing the home forward for modern life.

That is why I started Grouse.
For me, good joinery is not just about storage or finish. It is about how a room feels when you walk into it. The piece of furniture your eye is drawn to. The weight of a handle. The warmth of timber. The way a drawer opens. The feeling that something has been made specifically for the house, and for the people who live there.

Our aim is to create joinery that feels considered, useful and lasting. Work that improves how the room functions, respects the character of the property, and feels as though it has always belonged.
Thank you again for considering Grouse & Co for your project.

Adam Toms
Founder, Grouse & Co.

GROUSE
& COMPANY

JOINERY & INTERIORS
FOR BRITISH COUNTRY HOMES

Your Home In Context

ROTHERFIELD PEPPARD

Understanding the setting and history of a place helps us design and craft joinery that feels as though it has always belonged.




THE SETTING

Rotherfield Peppard is a village with agricultural roots stretching back centuries, historically formed of scattered farmsteads and cottages serving working estates.

During the late 17th century, as rural prosperity returned after the English Civil War, more substantial farmhouses began to appear.

Peppard Common became a focal point of village life, with homes positioned to overlook open grazing land and the cricket green, reflecting the traditional English pattern of settlement built around common ground.

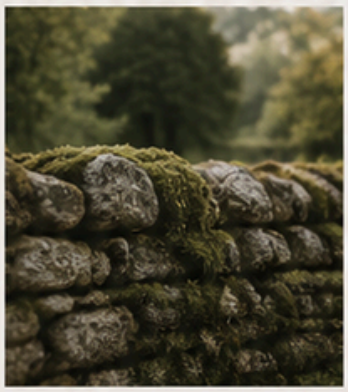





LAND & HERITAGE

Fields, commons and historic estates shape the character and rhythm of the village.

TIMELESS ARCHITECTURE

Houses reflect generations of craftsmanship and materials chosen to last.

NATURAL MATERIALS

Stone, brick, lime, oak and ironmongery create a sense of warmth, weight and authenticity.

VILLAGE CHARACTER

Quiet lanes, period homes and open spaces create a setting that feels both grounded and enduring.

EAST MANOR FARM

East Manor Farm has the character of a home that should be worked with carefully rather than overwritten.

Our approach will be to respect the existing proportions, details and atmosphere of the property while introducing practical, well-planned joinery for modern life.

That means considering scale, materials, shadow lines, hardware, colour, access and how each piece will feel in daily life.

The goal is simple: new work that feels useful, personal and settled, as though it belongs to the home rather than being added onto it.



info@grouseandcompany.co.uk
07555 604890
